


ID	Element	Task Type	Task Mode	Task Name	Duration	Start	Finish	<div><div><div>Half 1, 2027</div><div>Half 2, 2027</div><div>Half 1, 2028</div></div></div>																											
								D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J									
1		Construct	→	Preperation	2 days	Fri 1-1-27	Mon 4-1-27																												
2		Construct	→	Bring equipment and machinery	2 days	Fri 1-1-27	Mon 4-1-27																												
3		Construct	→	Placement of workmens shelter	2 days	Fri 1-1-27	Mon 4-1-27																												
4		Construct	→	Groundwork and Foundation	81 days	Tue 5-1-27	Tue 27-4-27																												
5		Construct	→	Prepare land for construction	20 days	Tue 5-1-27	Mon 1-2-27																												
6		Construct	→	measurements and coordination for foundation	4 days	Tue 2-2-27	Fri 5-2-27																												
7	20	Construct	→	Placing the foundation piles including pile caps	30 days	Mon 8-2-27	Fri 19-3-27																												
8		Construct	→	placing the formwork for foundation slab	3 days	Mon 22-3-27	Wed 24-3-27																												
9	11, 23	Construct	→	Pouring the concrete foundation slab	3 days	Thu 25-3-27	Mon 29-3-27																												
10		Construct	→	Curing of concrete foundation slab	7 days	Tue 30-3-27	Wed 7-4-27																												
11	25	Construct	→	Placing the parking walls, including the lift and stairway walls	7 days	Thu 8-4-27	Fri 16-4-27																												
12		Construct	→	Curing of walls	7 days	Mon 19-4-27	Tue 27-4-27																												
13		Construct	→	Structural building phase	166 days	Wed 28-4-27	Wed 15-12-27																												
14	22	Construct	→	Placing the columns on the foundation floor	14 days	Wed 28-4-27	Mon 17-5-27																												
15	26	Construct	→	Placing the stairs on the foundation floor	2 days	Wed 28-4-27	Thu 29-4-27																												
16	21	Construct	→	Placing the construction beams L1	14 days	Tue 18-5-27	Fri 4-6-27																												
17		Construct	→	placing the formwork for L1 flour	7 days	Mon 7-6-27	Tue 15-6-27																												
18	23	Construct	→	Pouring the L1 floor	3 days	Wed 16-6-27	Fri 18-6-27																												
19		Construct	→	Curing of L1 floor	7 days	Mon 21-6-27	Tue 29-6-27																												
20	25	Construct	→	Placing the walls L1	5 days	Wed 30-6-27	Tue 6-7-27																												






















Project: Planning-template  
Date: Wed 28-1-26


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Element	Task Type	Task Mode	Task Name	Duration	Start	Finish	Half 1, 2027							Half 2, 2027					Half 1, 2028						
								D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
21	22	Construct	➡	Place the collumns L1	5 days	Wed 30-6-27	Tue 6-7-27																			
22	26	Construct	➡	Placing the stairs on L1	2 days	Wed 30-6-27	Thu 1-7-27																			
23	21	Construct	➡	Placing the constrution beams L2	14 days	Wed 7-7-27	Mon 26-7-27																			
24	23, 28	Construct	➡	placing the L2 floor	5 days	Tue 27-7-27	Mon 2-8-27																			
25	25	Construct	➡	Placing the walls L2	5 days	Tue 3-8-27	Mon 9-8-27																			
26	22	Construct	➡	Place the collumns L2	5 days	Tue 3-8-27	Mon 9-8-27																			
27	26	Construct	➡	Placing the stairs on L2	2 days	Tue 3-8-27	Wed 4-8-27																			
28	21	Construct	➡	Placing the constrution beams L3	14 days	Tue 10-8-27	Fri 27-8-27																			
29	23, 28	Construct	➡	placing the L3 floor	5 days	Mon 30-8-27	Fri 3-9-27																			
30	25	Construct	➡	Placing the walls L3	5 days	Mon 6-9-27	Fri 10-9-27																			
31	22	Construct	➡	Place the collumns L3	5 days	Mon 6-9-27	Fri 10-9-27																			
32	26	Construct	➡	Placing the stairs on L3	2 days	Mon 6-9-27	Tue 7-9-27																			
33	21	Construct	➡	Placing the constrution beams L4	14 days	Mon 13-9-27	Thu 30-9-27																			
34	23, 28	Construct	➡	placing the L4 floor	5 days	Fri 1-10-27	Thu 7-10-27																			
35	25	Construct	➡	Placing the walls L4	5 days	Fri 8-10-27	Thu 14-10-27																			
36	22	Construct	➡	Place the collumns L4	5 days	Fri 8-10-27	Thu 14-10-27																			
37	26	Construct	➡	Placing the stairs on L4	2 days	Fri 8-10-27	Mon 11-10-27																			
38	21	Construct	➡	Placing the constrution beams L5	14 days	Fri 15-10-27	Wed 3-11-27																			
39	23, 28	Construct	➡	placing the L5 floor	5 days	Thu 4-11-27	Wed 10-11-27																			
40	25	Construct	➡	Placing the walls L5	5 days	Thu 11-11-27	Wed 17-11-27																			
41	22	Construct	➡	Place the collumns L5	5 days	Thu 11-11-27	Wed 17-11-27																			
42	26	Construct	➡	Placing the stairs on L5	2 days	Thu 11-11-27	Fri 12-11-27																			

Project: Planning-template  
Date: Wed 28-1-26





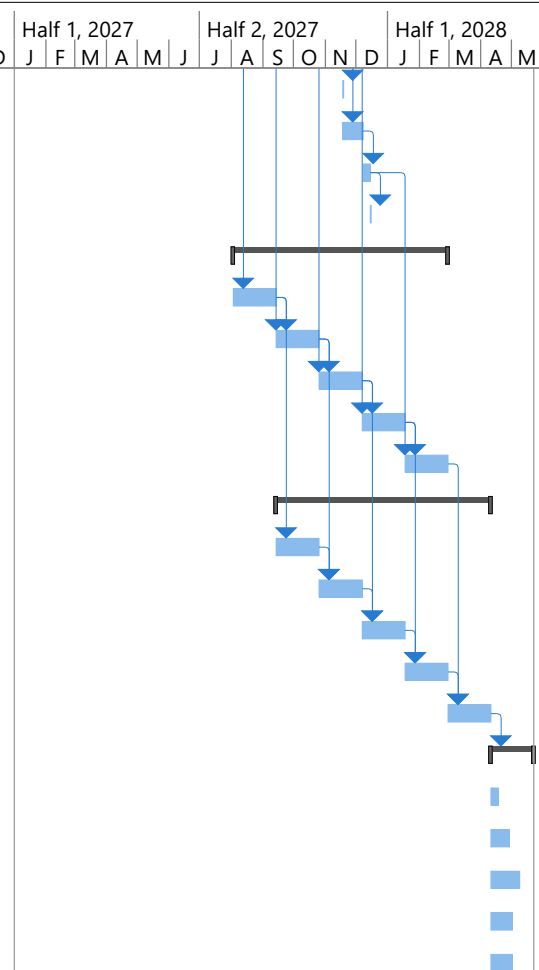




Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Element	Task Type	Task Mode	Task Name	Duration	Start	Finish	Half 1, 2027							Half 2, 2027				Half 1, 2028																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
								D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
43	24	Construct	→	Place the lift	1 day	Thu 18-11-2	Thu 18-11-27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				



Project: Planning-template  
Date: Wed 28-1-26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID	Element	Task Type	Task Mode	Task Name	Duration	Start	Finish	Half 1, 2027							Half 2, 2027					Half 1, 2028						
								D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
65	42	Construct		tree	20 days	Tue 11-4-28	Mon 8-5-28																			
66	44	Construct		pergola	5 days	Tue 11-4-28	Mon 17-4-28																			
67	45	Construct		planten	15 days	Tue 2-5-28	Mon 22-5-28																			
68	46	Construct		planter box	15 days	Tue 11-4-28	Mon 1-5-28																			
69	51	Construct		shrank	15 days	Tue 11-4-28	Mon 1-5-28																			
70	52	Construct		table/ chairs	10 days	Tue 11-4-28	Mon 24-4-28																			
71	53	Construct		trash	1 day	Tue 11-4-28	Tue 11-4-28																			
72	54	Construct		towel	1 day	Tue 11-4-28	Tue 11-4-28																			
73	12	Construct		Road stripping	1 day	Tue 11-4-28	Tue 11-4-28																			




Project: Planning-template

Date: Wed 28-1-26


Task




Inactive Summary




External Tasks




Split




Manual Task




External Milestone




Milestone




Duration-only




Deadline




Summary




Manual Summary Rollup




Progress




Project Summary




Manual Summary




Manual Progress




Inactive Task



Start-only



Inactive Milestone



Finish-only

